



ID	Task Name	Start	Finish	2009				2010				2011				2012				2013			
				Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
30	<b>NEW SCHOOLS</b>	<b>Mon 10/2/06</b>	<b>Fri 6/28/13</b>																				
31	Projects Start	Mon 10/2/06	Mon 10/2/06																				
32	Linda Jobe Middle School No. 6 (Prototype)	Wed 10/4/06	Fri 11/13/09																				
105	Asa E Low Jr. Intermediate School No. 6	Mon 10/23/06	Fri 11/13/09																				
166	Annette Perry Elementary Schools No. 21	Tue 5/15/07	Tue 12/15/09																				
209	Lake Ridge High School	Wed 7/18/07	Wed 6/20/12																				
210	Design	Wed 7/18/07	Fri 4/3/09																				
263	Bid and Award HS 5 Onsite, Offsite Work	Tue 2/17/09	Tue 7/28/09																				
272	Construction and Offsite Detention, Sewer, Road	Mon 7/13/09	Wed 6/20/12																				
273	Notice to Proceed	Mon 7/13/09	Mon 7/13/09																				
274	Construct Offsite Detention, Site Fill	Tue 7/14/09	Tue 3/2/10																				
281	Underground (UG) Utilities Site and Offsite	Tue 11/17/09	Wed 3/23/11																				
289	Construct Building Facilities	Thu 8/27/09	Wed 4/11/12																				
309	Athletic Facilities	Mon 2/15/10	Fri 3/30/12																				
328	Site Lighting, Irrigation, Landscape	Mon 12/13/10	Tue 4/10/12																				
332	Day Miar Road Frontage Improvements (LS-LF)	Mon 3/5/12	Wed 4/11/12																				
333	Float Time Allowance	Thu 4/12/12	Wed 5/30/12																				
334	Move-in & Final Completion	Thu 5/31/12	Wed 6/20/12																				
335	Nancy Neal Elementary School No. 23	Thu 5/17/07	Fri 8/19/11																				
384	Judy K. Miller Elementary School No. 22 (2013)	Thu 5/17/07	Fri 6/28/13																				
385	Design	Thu 5/17/07	Fri 12/30/11																				
403	Bid and Award	Mon 1/9/12	Fri 3/2/12																				
412	Construction	Mon 3/5/12	Fri 6/28/13																				
413	Notice to Proceed	Mon 3/5/12	Mon 3/5/12																				
414	Substantial Completion Work	Tue 3/6/12	Tue 4/30/13																				
415	Float Time Allowance	Wed 5/1/13	Fri 5/31/13																				
416	Move-in & Final Completion	Mon 6/3/13	Fri 6/28/13																				
417	<b>CAPITAL MAINTENANCE PROJECTS</b>	Mon 6/3/02	Mon 6/3/02																				
418	Capital Maintenance	Wed 6/28/06	Fri 2/22/08																				
549	<b>INFRASTRUCTURE PROJECTS</b>	Mon 6/3/02	Mon 6/3/02																				
550	HVAC Automation and Sensors (12 Schools)	Wed 6/28/06	Fri 2/29/08																				
578	6th Avenue Bus Transport Facility	Mon 9/25/06	Wed 12/31/08																				
605	Della Icenhower Access Road to South Collins	Wed 3/30/11	Mon 4/30/12																				
606	Execute A/E Agreement	Wed 3/30/11	Wed 3/30/11																				
607	Design	Wed 4/13/11	Mon 8/1/11																				
617	Bid	Mon 8/15/11	Tue 9/27/11																				
624	Construction	Mon 10/3/11	Mon 4/30/12																				
625	Notice To Proceed	Mon 10/3/11	Mon 10/3/11																				
626	Construct Access Drive and Sidewalk with Collins Road	Thu 3/1/12	Mon 4/30/12																				
627	Liason COA and Lacy Construction for Approach Work	Tue 8/2/11	Mon 9/19/11																				

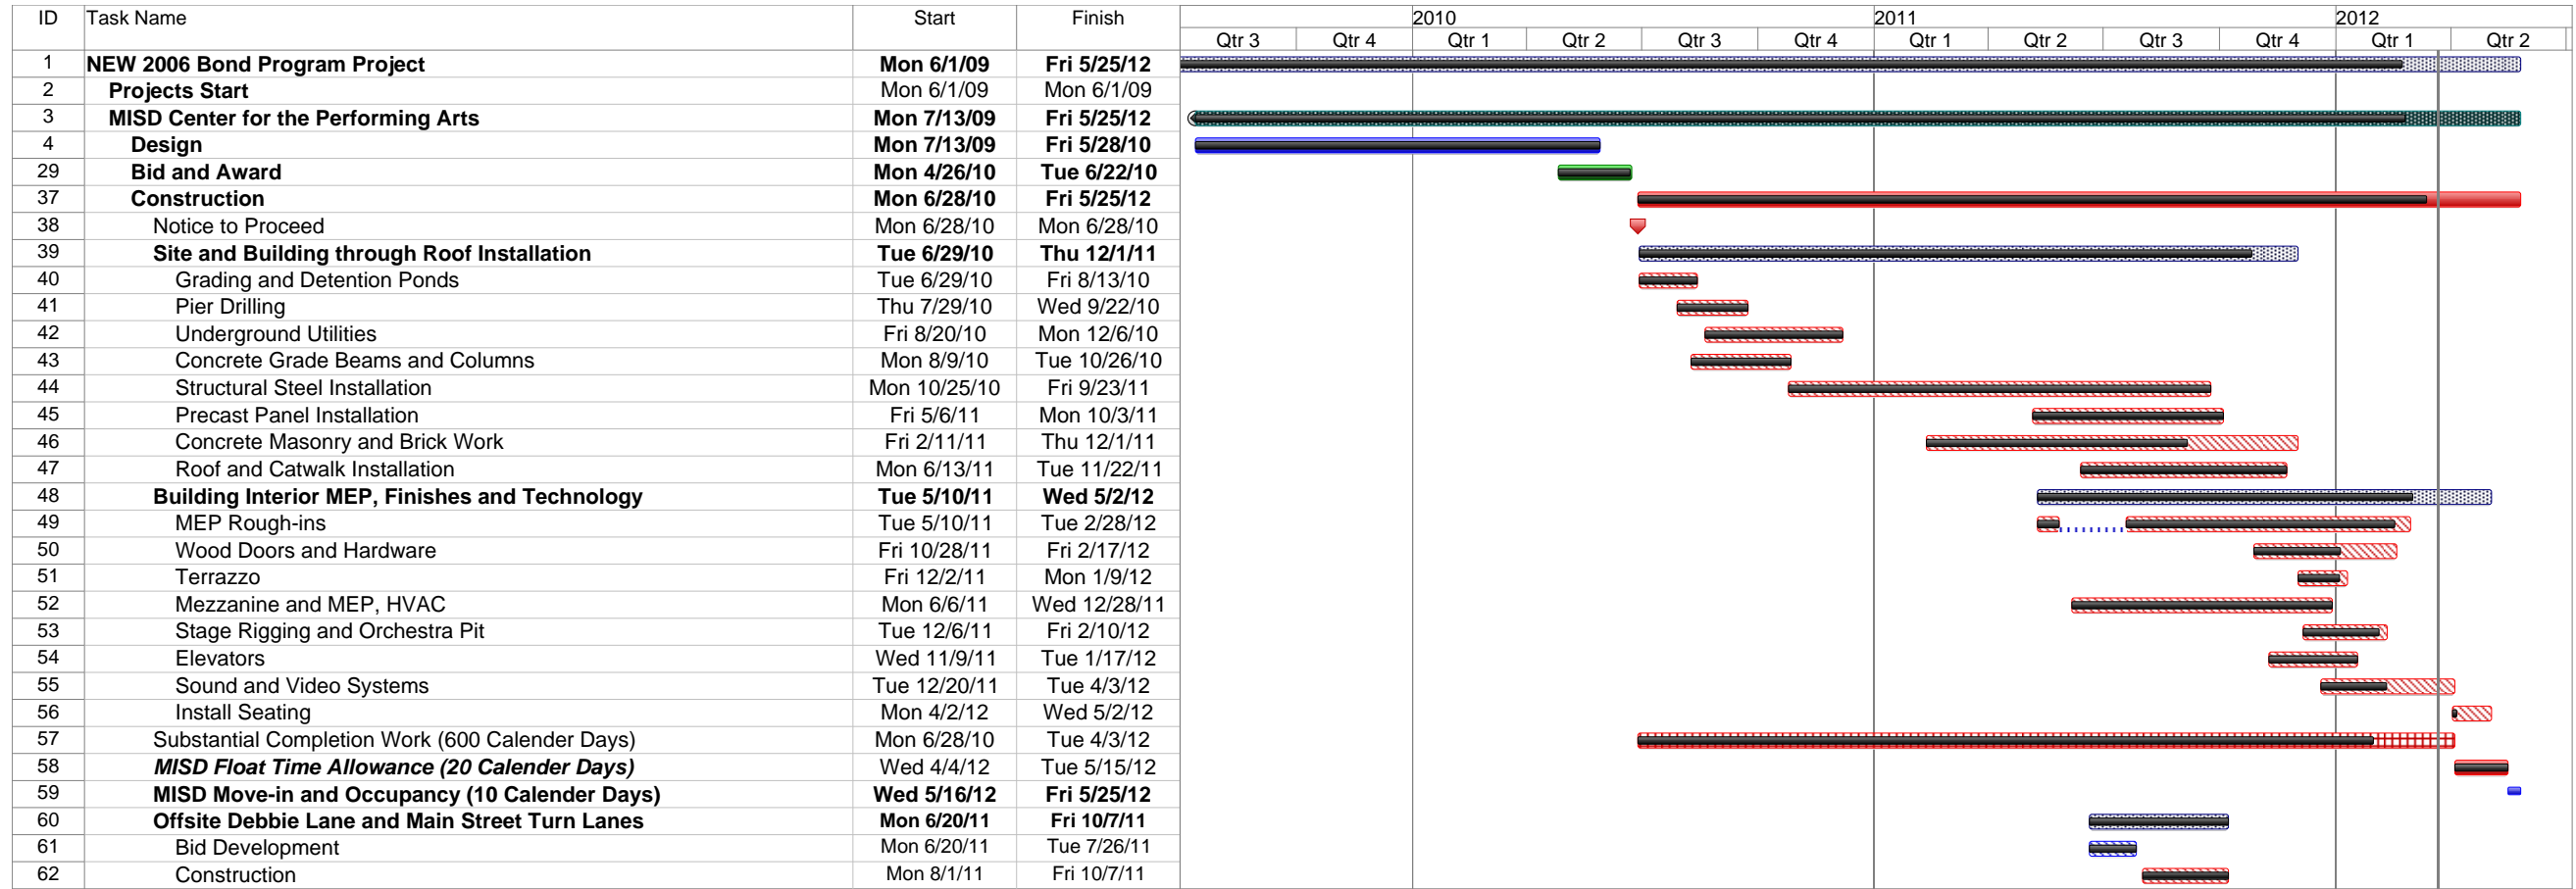

Mansfield ISD 2006 Bond Program

Sixth Avenue Bus Parking Addition

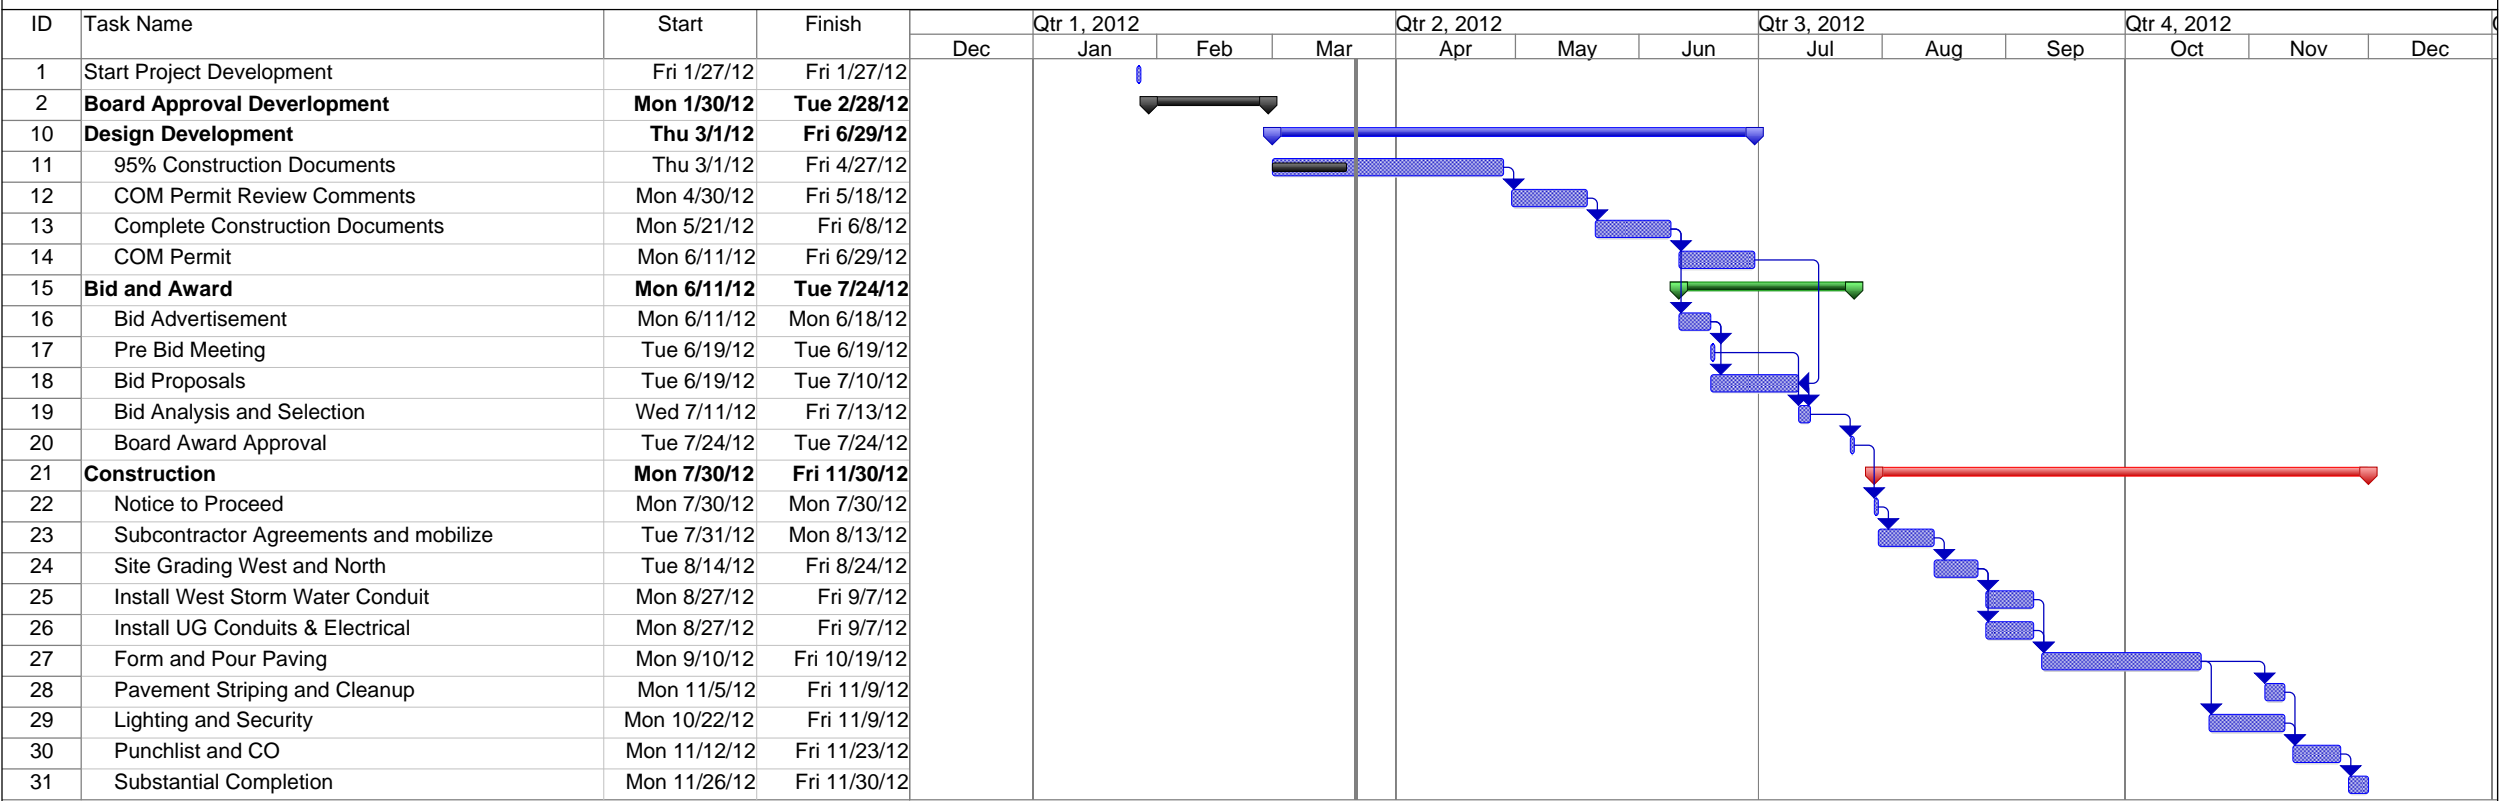

Project: 6th Ave Bus Parking Addition]  
Date: Thu 3/22/12

Task		External Tasks		Inactive Summary		Start-only	
Split		External Milestone		Manual Task		Finish-only	
Milestone		Inactive Task		Duration-only		Progress	
Summary		Inactive Task		Manual Summary Rollup		Deadline	
Project Summary		Inactive Milestone		Manual Summary			
