


JL Boren (105) and Alice Ponder (101) Elementary Schools

Schedule Summary

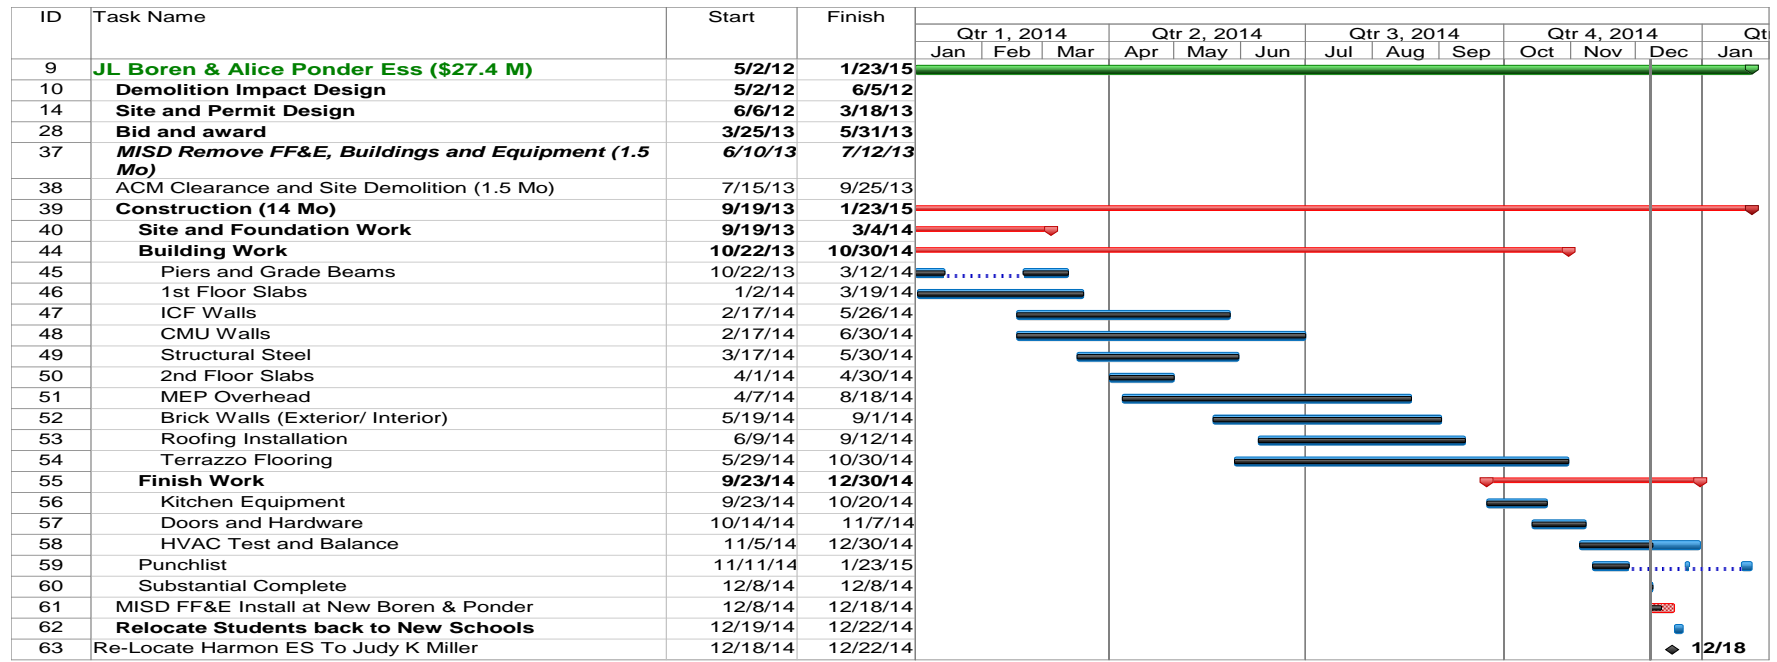

Cost Summary

Contract Award Amount: \$27,400,000

Change Order Amount: \$182,099.00

Contract Amount: \$27,582,099.00

Status Summary

1. JL Boren ES; Installation of the Irrigation system and Landscaping is complete. Substantial Completion for the Building only was issued on Monday, December 8, 2014. Classroom and Office Furniture as well as the relocation of FF & E items from Judy K Miller ES to new Boren ES was completed over Winter Break. The General Contractor is progressing with Punch List and Warranty Work order process.
2. Alice Ponder ES; Installation of the Irrigation system and Landscaping is complete. Substantial Completion for the Building only was issued on Monday, December 8, 2014. Classroom and Office Furniture as well as the relocation of FF & E items from old Tarver-Rendon ES to new Alice Ponder ES was completed over Winter Break. The General Contractor is progressing with Punch List and Warranty Work order process.
